

Georgia Department of Human Resources
**APPLICATION FOR CONSTRUCTION PERMIT AND SITE APPROVAL
 FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM**


Subdivision, Street or Road <i>The Bluffs S/D Lot # 13</i>		Health District <i>02</i>	County <i>Hall</i>
Property Location (Address, Block, Lot, Directions to Property) <i>light off Thompson Bridge on Cochran 4120 Willow Trace Gainesville 3</i>			
I hereby apply for a construction permit to install or construct an individual sewage disposal system and agree that the system will be installed to conform to the requirements of the rules of the former Georgia Department of Public Health, Chapter 270-5-25 now assigned to the Division of Physical Health. I understand that final inspection is required and will notify the local or State Department upon completion of construction and before applying final cover.			
Signature (Owner or Applicant) <i>Mark Bell</i>		Date <i>12-2-80</i>	
Property Owner's Name <i>Mark Bell</i>		MUST BE INSPECTED CALL 532-5241	
Owner's Address			
Permit Applicant's Name <i>W. J. Gross Co.</i>		Phone No. [REDACTED]	
Applicant's Address <i>P.O. Box 2302 Gainesville, Ga.</i>			
Financial Assistance <input type="checkbox"/> FHA, <input type="checkbox"/> VA, <input type="checkbox"/> Farmers Home, <input checked="" type="checkbox"/> Conventional, Case Number _____			
Type Facility (Residence, Church, Motel, Restaurant, Etc.) <i>Residence</i>		No. of Bedrooms or No. of Cottages Per Day <i>3</i>	
Water Supply <input checked="" type="checkbox"/> Public, <input type="checkbox"/> Community, <input type="checkbox"/> Individual		Located Required Distances From Possible Pollution Source <input type="checkbox"/> Yes, <input type="checkbox"/> No	
Lot Size Front <i>60</i> Ft., Rear <i>130</i> Ft., Right Side <i>238</i> Ft., Left Side <i>200</i> Ft., Square Ft./Acre _____			
House Design <input type="checkbox"/> Ground Level, <input type="checkbox"/> Split Level, <input checked="" type="checkbox"/> With Basement		Level of Plumbing Outlet <input type="checkbox"/> Ground Level, <input type="checkbox"/> Split Level, <input checked="" type="checkbox"/> Basement	
Soil Conditions (Nitrification Field) Percolation Rate <i>28</i> Min./in.; Water Table Depth _____ Feet; Soil Type (Rock, Etc.) _____			
Sewage Disposal <input checked="" type="checkbox"/> Septic Tank, <input type="checkbox"/> Construction Privy, <input type="checkbox"/> Pit Privy		Total Capacity Septic Tank <i>1000</i> Gals., Dosing Tank _____ Gals., Grease Trap _____ Gals.	
Field Layout Method <input type="checkbox"/> Distribution Box, <input type="checkbox"/> Level Field, <input checked="" type="checkbox"/> Serial Distribution		Nitrification Field Area Total Sq. Ft. <i>729</i> ; Total Linear Ft. <i>243</i> ; Trench Width In. <i>36</i>	
If Distribution Box is Used No. of Lines _____; Length Each Line, Ft. _____			
Site Approved <input type="checkbox"/> Yes, <input type="checkbox"/> No		MUST BE COUNTERSIGNED BY BONDED SEWAGE SYSTEM CONTRACTOR PRIOR TO CONSTRUCTION OF SEWAGE SYSTEM.	
Special Conditions (Explain)		SIGNED: <i>Hart Gook</i> BONDED SEPTIC TANK CONTRACTOR	
SUBJECT TO OFFICIAL APPROVAL OF HALL CO. PLANNING COMMISSION BEFORE BEGINNING CONSTRUCTION <i>12/11/89 copy to northeast in Beltsville</i> PERMIT			
A Permit is hereby granted to install or construct the individual sewage disposal system described above. This Permit is not valid unless properly signed below, and expires twelve (12) months from date of issue.			
Construction Permit Number <i>7997</i>		Date of Issue <i>12/2/80</i>	
Approved by (Health Department Representative) <i>A. C. Shallege</i>		Title	

3-24-81 2:00 Gook


92
102
54

248'

G-111
3-24-81
2:40 PM

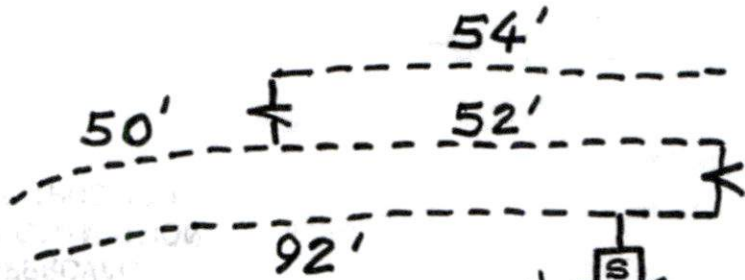

GRAVEL OK

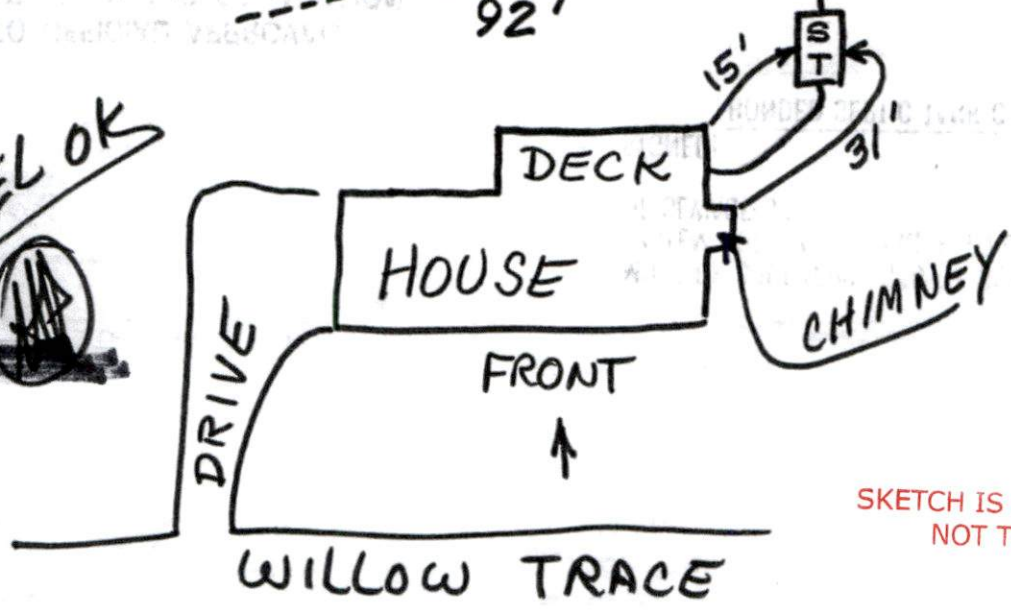

SKETCH IS APPROXIMATE
NOT TO SCALE

DATE 233-2511
WORLD BE IMPROVED
