


Subdivision: Dier Ridge Phase/section: _____ Lot# 8 Installer: Jeff Paterson
 Water Supply: Private Well Spring Shared Well Community Min. Required Separation Distance 5' Installed? Yes No

Conditions: 1) Pump septic tank every 3 to 5 years. 2) Divert all gutters and other surface water, away from septic system and repair areas. (3) No cutting or filling over septic system and repair areas.

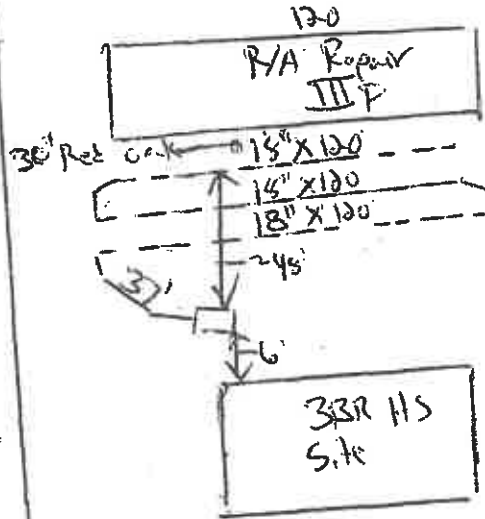

(Well Area)

Operations Permit For: New System Repair Revision Drawings, plans, conditions, etc. attached? Yes No
 System Approved For: House Mobile Home (single double) Bedrooms: 3 Basement: Yes No Basement Plumbing: Yes No
 Multiple Unit Dwelling: No. of Units _____ Number of Bedrooms per unit _____ Business No. Employees: _____ No. Shifts: _____

Operation Description: _____ Industrial Waste: Yes No
 Approved Installation Specifications: 360 (GPD) 0.45 System Classification: Type I, II, III, IV, V, VI
 Pump System Required: Yes No Empty Pump Make: _____ Model: _____ Serial No. _____
 Trenches: Length: 20 ft No. of Trenches 3 Width: 18" Spacing: 7.5 ft Depth: 18 in (lower sidewall) Stone Depth: _____ in
 Equal Gravity Pressure Manifold Serial Dams/Step Downs 1000 (gallons) Pump Tank: _____ (gallons)
 Prefabricated Panel Block Conventional Large Diameter Pipe Chamber Expanded Polystyrene Aggregate Other _____

Comments: _____
 Inspected by: Ch... Date: 11/26/07 Issued To: M. Paterson Date: _____

The system has been installed in accordance with state sewage rules. Approval does not guarantee the system will function satisfactory for any given time.
 Oprpmt.doc.rev 03/05/04
