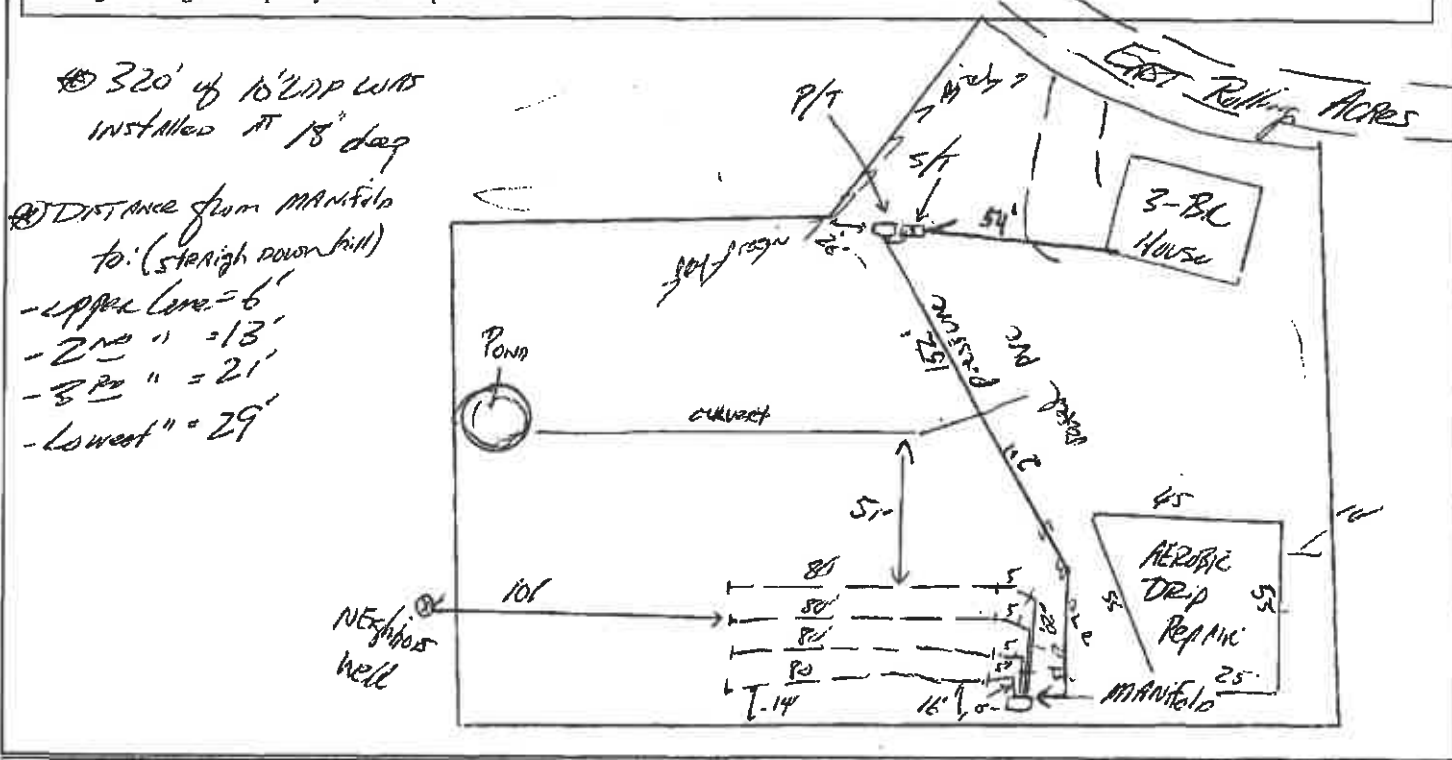


Case Number: SEP 2015-01467BUNCOMBE COUNTY HEALTH CENTER
ENVIRONMENTAL HEALTH SERVICES (828-250-1166)
OPERATIONS PERMITPIN: 9733506646Property Owner: Ryan and Monica LeBlanc Property Location: 10 East Rolling Acres Application Date: 11-24-15Directions: 25/90 towards Marshall (L) Monticello (R) Rolling Acres SVA - take first (R) to #10 (L).Subdivision: _____ Phase/section: _____ Lot#: _____ Installer: Rust, (John) Lipe #1524Water Supply: ☐ Private Well ☐ Spring ☐ Shared Well ☒ Community Min. Required Separation Distance _____ Installed? ☐ Yes ☒ No

Conditions: 1) Pump septic tank every 3 to 5 years. 2) Divert all gutters and other surface water, away from septic system and repair areas. (3) No cutting or filling over septic system and repair areas.

Operations Permit For: ☒ New System ☐ Repair ☐ Revision Drawings, plans, conditions, etc. attached? ☐ Yes ☒ NoSystem Approved For: ☒ House ☐ Mobile Home (☐ single ☐ double) Bedrooms: 3 Basement: ☐ Yes ☒ No Basement Plumbing: ☐ Yes ☐ No☐ Multiple Unit Dwelling: No. of Units _____ Number of Bedrooms per unit _____ ☐ Business No. Employees: _____ No. Shifts: _____

Operation Maintenance & Monitoring Description (if applicable): _____

Industrial Waste: Yes ☐ No ☒Approved Installation Specifications: Total Design Flow: 360 LTAR: 0.45 System Classification: Type I, II, III, IV, V, VI (GPD)Pump System Required: ☒ Yes ☐ No Pump Specification Pump Make: Liberty Model: _____ Serial No. _____Trenches: Length: 320 ft No. of Trenches 4 Width: 18" Spacing: 8 ft Depth: 18" in (lower sidewall) Stone Depth: _____ inDistribution: ☐ Equal Gravity ☒ Pressure Manifold ☐ Serial ☐ Dams/Step Downs Tank Size: Septic: 1000 Pump Tank: 1200 (gallons) (gallons)System Type Installed: ☐ Prefabricated Panel Block ☐ Conventional ☒ Large Diameter Pipe ☐ Chamber ☐ Expanded Polystyrene Aggregate ☐ Other _____Comments: Pump & Septic Tanks = Infiltrator S+B 2071-1060 P# 2077-1060
Checked pump cycle 10/11/16 RKLInspected by: Richard K. Blah Date: 10/11/16 Issued To: Rust, (John) Lipe Date: 10/14/16

The system has been installed in accordance with state sewage rules. Approval does not guarantee the system will function satisfactory for any given time.
